

CITIZEN'S OVERSIGHT COMMITTEE



Measure T Projects

June 29, 2022



Measure T (County Regional Projects):

Avenue 26/Road 29 Rehabilitation

Road 200 Phase 3 Bridge

Avenue 7 Rehabilitation (west of SR 99)

Measure T (General Road Maintenance):

Pothole patching, shouldering, drainage maintenance

Supplement road maintenance funds


Measure T (Road Maintenance Districts):

Various treatments (overlays, seals, etc.)

Matched with MD funds

Avenue 26/Road 29 Rehabilitation

- 16 miles of road rehabilitation
- Avenue 26 from Chowchilla City Limit to Road 29; Road 29 from Avenue 26 to Eastman Lake entrance
- Federal Land Access Program (FLAP): \$22M (88.7%)
+ Measure T: \$2.8M (11.3%)
- Project bid on 11/16/2021
- Project Awarded on 12/14/2021: \$16.7M contract to Granite Construction
- **UNDER CONSTRUCTION!!**
- Estimated completion: December 2022

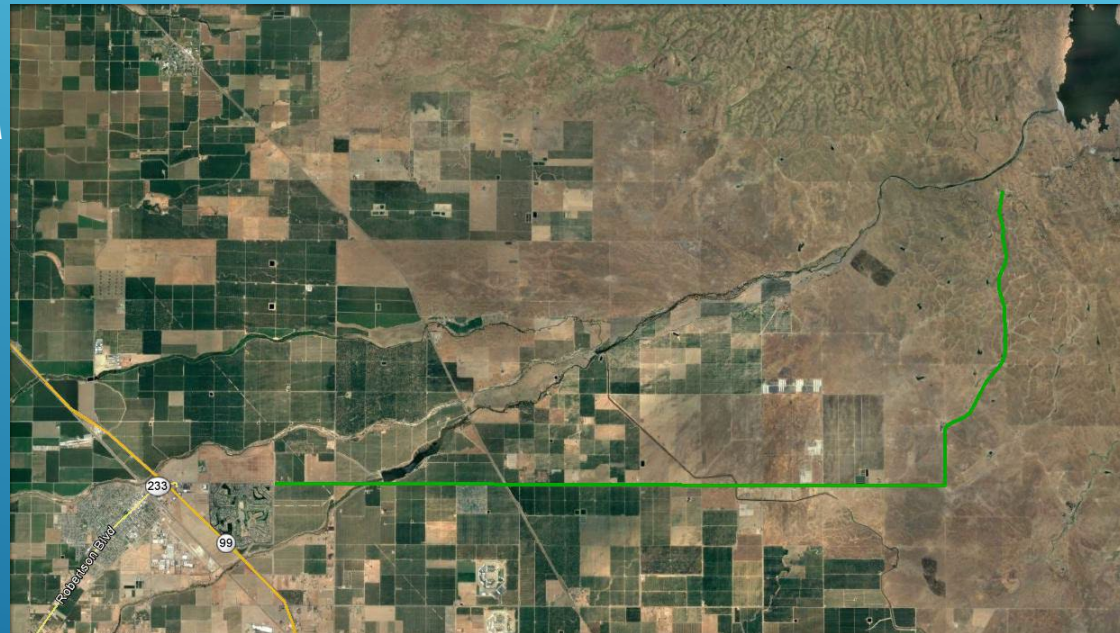

Avenue 26/Road 29 Rehabilitation

- Roadway pulverizing



Avenue 26/Road 29 Rehabilitation

- Subgrade excavation/preparation



Avenue 26/Road 29 Rehabilitation

- Roadway paving



Road 200 Phase 3 Bridge

- Re-align road and replace bridge at Finegold Creek
- Funded by combination of MCTC Regional Measure T and County Regional Measure T
- Project bid on 2/22/22
- Project Awarded on 4/5/22: \$9.3M contract to MCM
- **UNDER CONSTRUCTION!!**
- Estimated completion: May 2023



Road 200 Phase 3 Bridge

- Roadway approach excavation



Road 200 Phase 3 Bridge

- Bridge abutment excavation



Road 200 Phase 3 Bridge

- Bridge abutment footing forming




Avenue 7 Rehabilitation (west of SR 99)

- 2 miles of road rehabilitation (Road 30-1/2 to SR 99)
- Measure T: \$1.3M (67%) + SB-1 Local Partnership Program (formula): \$660K (33%)
- Project bid on 5/5/2022
- Project Awarded on 5/24/2022: \$2M contract to Yarbs Paving & Grading, Inc. (grouped with SB-1 projects for cost savings benefit)

- **CONSTRUCTION START
ANTICIPATED AUG/SEPT 2022**

**Completes the 6-mile segment of Ave 7 from SR 145 to SR 99

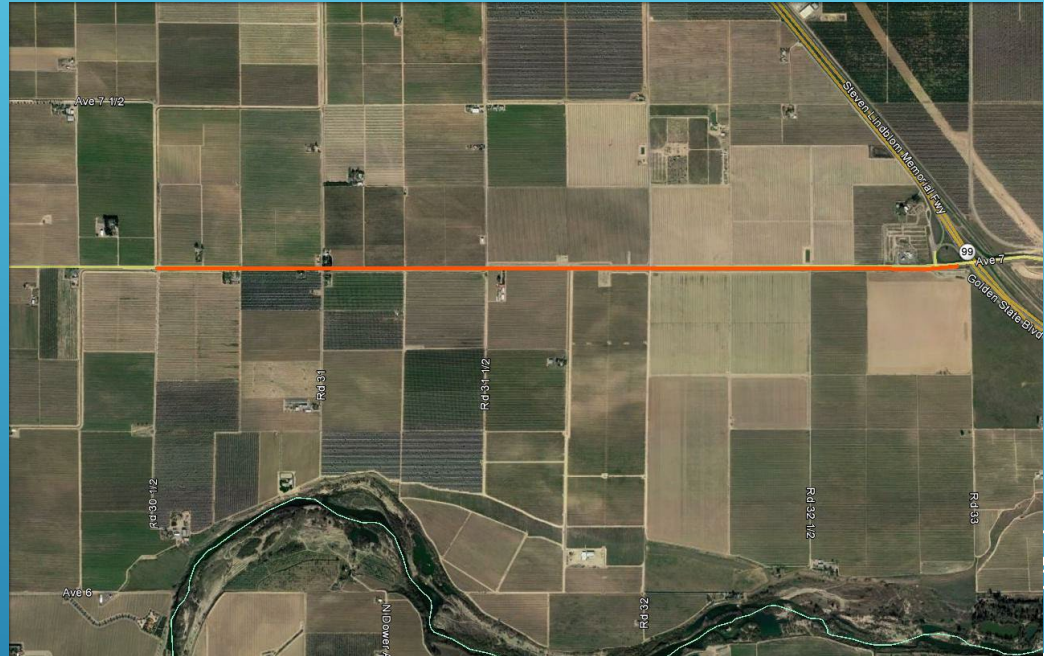

River Parkway Rd (aka Oakhurst Midtown Connector)



River Parkway Rd (aka Oakhurst Midtown Connector)



River Parkway Rd (aka Oakhurst Midtown Connector)



River Parkway Rd (aka Oakhurst Midtown Connector)



River Parkway Rd (aka Oakhurst Midtown Connector)



River Parkway Rd (aka Oakhurst Midtown Connector)



Pavement Management System

- Continual evaluation and update of database of all county road conditions (1,507 county-maintained miles)





CONTACT PUBLIC WORKS
(559) 675-7811

Questions?

